

**LARAMIE COUNTY
NOTICE OF AWARD**

April 3, 2024

Simon Contractors
Attn: Mr. Rob Meidinger
PO Box 20150
Cheyenne, Wyoming 82003

Dear Mr. Meidinger:

Laramie County, having duly considered the proposals submitted on March 20, 2024, for the construction of the COUNTY ROAD 142 RECONSTRUCTION project as outlined in the Contract Documents, and it appears that your Proposal for performing the work outlined is fair, equitable, and in the best interest of the County, the bid items are hereby accepted at the bid prices contained therein.

In accordance with the terms of the Contract Documents, you are required to execute the formal Agreement and furnish the required Performance and Payment bonds within fifteen (15) consecutive calendar days from and including the date of this Notice.

In addition, you are required to furnish at the same time a copy of Certificate of Insurance evidencing compliance with the requirements for insurance stated in the Contract Documents and a copy of your Worker's Compensation Certificate.

The Bid Guarantee submitted with your Proposal will be retained until the Agreement has been executed and the required Performance and Payment Bonds have been furnished and approved. In the event that you should fail to execute the Contract and furnish the Performance and Payment Bonds within the time limit specified, the said Bid Security will be retained as liquidated damages and not as penalty for the delay and extra work caused thereby.

LARAMIE COUNTY

By: _____

Title: _____

RECEIVED AND APPROVED AS

ONLY BY THE
DEPUTY LARAMIE COUNTY
ATTORNEY *RID*



BenchMark

ENGINEERS, P.C.

Quality minded, community spirited.

March 21, 2024

Ms. Molly Bennett, Director
Laramie County Public Works
13797 Prairie Center Circle
Cheyenne, WY 82009

RE: County Road 142 Reconstruction

Dear Ms. Bennett:

BenchMark Engineers, P.C. (BME) has reviewed the bids submitted on March 20, 2024 for the above-referenced project. Two bids were received for this project; one from Knife River and one from Simon Contractors. Simon Contractors of Cheyenne submitted the lowest responsible bid in the amount of \$5,189,321.50. All necessary documentation was included with the two bids submitted.

It is our recommendation that Laramie County accept the bid in the amount of \$5,189,321.50 from Simon Contractors. This work will include full depth reclamation, earthwork and grading, installation of culverts, asphalt paving, road striping and other associated work on approximately 4.9 miles of County Roads 142, 215A, and 143.

The Notice of Award, that is to be completed by the County Commissioners, and a tabulation of the bids submitted are included with this letter. Please contact us if you have any questions regarding our recommendation or require additional information.

Sincerely,

A handwritten signature in blue ink, appearing to read "Scott D. Larson", is written over a blue horizontal line.

Scott D. Larson, P.E.
President

Enclosures:

Bid Tabulation
Notice of Award

County Road 142 Reconstruction Bid Tabulation

Item No.	Specification Section	Description	Unit	Estimated Quantity	Simon Contractors		Knife River		Engineer's Estimate	
					Unit Price	Total Cost	Unit Price	Total Cost	Unit Price	Total Cost
1	04001 SP	Mobilization	LS	1	\$203,000.00	\$203,000.00	\$348,000.00	\$348,000.00	\$492,900.00	\$492,900.00
2	N/A	Bonds and Insurance	LS	1	\$24,500.00	\$24,500.00	\$19,300.00	\$19,300.00	\$59,400.00	\$59,400.00
3	04002 SP	Traffic Control and Site Safety	LS	1	\$171,200.00	\$171,200.00	\$180,000.00	\$180,000.00	\$296,900.00	\$296,900.00
4	04003 SP	Quality Control Testing	LS	1	\$35,500.00	\$35,500.00	\$56,900.00	\$56,900.00	\$89,100.00	\$89,100.00
5	N/A	Utility Potholing	EA	26	\$1,000.00	\$26,000.00	\$1,700.00	\$44,200.00	\$1,200.00	\$31,200.00
6	Addendum 1	Variable Message Signs (VMS)	DAY	90	\$140.00	\$12,600.00	\$160.00	\$14,400.00	\$200.00	\$18,000.00
7	Addendum 1	Flagging	HR	500	\$48.00	\$24,000.00	\$51.00	\$25,500.00	\$55.00	\$27,500.00
8	Addendum 1	Pilot Car	DAY	60	\$850.00	\$51,000.00	\$910.00	\$54,600.00	\$1,000.00	\$60,000.00
9	Addendum 1	Motor Grader Hours	HR	150	\$275.00	\$41,250.00	\$180.00	\$27,000.00	\$215.00	\$32,250.00
10	02050 SP	Remove Culvert	LF	1,170	\$29.00	\$33,930.00	\$35.00	\$40,950.00	\$25.00	\$29,250.00
11	04006 SP	Remove Delineators	LS	1	\$107.00	\$107.00	\$114.00	\$114.00	\$3,000.00	\$3,000.00
12	02805 SP	Remove Sign (return to owner)	EA	10	\$273.00	\$2,730.00	\$290.00	\$2,900.00	\$200.00	\$2,000.00
13	02805	Remove & Reset Sign	EA	18	\$778.00	\$14,004.00	\$825.00	\$14,850.00	\$500.00	\$9,000.00
14	02050	Remove Concrete Approach	SY	100	\$36.50	\$3,650.00	\$28.00	\$2,800.00	\$20.00	\$2,000.00
15	02075 SP	Transition Section	EA	2	\$2,700.00	\$5,400.00	\$4,129.00	\$8,258.00	\$3,500.00	\$7,000.00
16	04004 SP	Full Depth Reclamation	SY	88,000	\$2.00	\$176,000.00	\$1.30	\$114,400.00	\$2.00	\$176,000.00
17	04004 SP	Stabilized Full Depth Reclamation	SY	2,400	\$12.00	\$28,800.00	\$22.00	\$52,800.00	\$6.00	\$14,400.00
18	Addendum 1	Topsoil Stripping	LS	1	\$67,000.00	\$67,000.00	\$93,285.00	\$93,285.00	\$40,000.00	\$40,000.00
19	02210	Unclassified Excavation	CY	31,000	\$9.70	\$300,700.00	\$6.40	\$198,400.00	\$7.00	\$217,000.00
20	02231 SP	Crushed Base, 6" (for approaches)	Ton	700	\$29.50	\$20,650.00	\$76.00	\$53,200.00	\$44.00	\$30,800.00
21	02231 SP	Crushed Base, 6" (for mainline roads)	Ton	36,000	\$29.50	\$1,062,000.00	\$33.65	\$1,211,400.00	\$40.00	\$1,440,000.00
22	02231 SP	Crushed Base, 6" (surfacing)	Ton	820	\$29.50	\$24,190.00	\$74.00	\$60,680.00	\$44.00	\$36,080.00
23	02190 SP	Crushed Base (shoulder material)	Ton	800	\$35.00	\$28,000.00	\$74.00	\$59,200.00	\$50.00	\$40,000.00
24	02512 SP	Plant Mix Bit. Pavement, 3" (for approaches)	Ton	400	\$223.00	\$89,200.00	\$180.50	\$72,200.00	\$180.00	\$72,000.00
25	02512 SP	Plant Mix Bit. Pavement, 4" (for mainline roads)	Ton	22,400	\$102.50	\$2,296,000.00	\$116.90	\$2,618,560.00	\$145.00	\$3,248,000.00
26	02776 SP	Concrete Approach, 6"	SY	65	\$148.00	\$9,620.00	\$143.00	\$9,295.00	\$140.00	\$9,100.00
27	02725	18" CMP Culvert	LF	1,070	\$67.00	\$71,690.00	\$71.00	\$75,970.00	\$78.00	\$83,460.00
28	02725	24" CMP Culvert	LF	860	\$87.00	\$74,820.00	\$92.00	\$79,120.00	\$125.00	\$107,500.00
29	02725	36" CMP Culvert	LF	150	\$131.00	\$19,650.00	\$139.00	\$20,850.00	\$205.00	\$30,750.00
30	02725	18" CMP FES	EA	38	\$402.00	\$15,276.00	\$426.00	\$16,188.00	\$400.00	\$15,200.00

31	02725	24" CMP FES	EA	24	\$615.25	\$14,766.00	\$653.00	\$15,672.00	\$750.00	\$18,000.00
32	02725	36" CMP FES	EA	4	\$1,605.00	\$6,420.00	\$1,700.00	\$6,800.00	\$1,500.00	\$6,000.00
33	02805 SP	Sign, Single Post	EA	11	\$909.50	\$10,004.50	\$966.00	\$10,626.00	\$800.00	\$8,800.00
34	02805 SP	Sign, Double Post	EA	2	\$1,350.00	\$2,700.00	\$1,400.00	\$2,800.00	\$1,400.00	\$2,800.00
35	02805 SP	Stop Sign with Solar Powered Flashing Beacon	EA	2	\$6,420.00	\$12,840.00	\$6,800.00	\$13,600.00	\$3,000.00	\$6,000.00
36	02900	Dryland Seed	Acre	16.3	\$1,450.00	\$23,635.00	\$1,500.00	\$24,450.00	\$2,800.00	\$45,640.00
37	04005 SP	Striping, Edge Line	Mile	9.70	\$1,450.00	\$14,065.00	\$1,500.00	\$14,550.00	\$2,700.00	\$26,190.00
38	04005 SP	Striping, Centerline	Mile	4.88	\$1,050.00	\$5,124.00	\$1,135.00	\$5,538.80	\$2,700.00	\$13,176.00
39	04005 SP	Railroad Crossing Markings	EA	2	\$3,210.00	\$6,420.00	\$3,400.00	\$6,800.00	\$2,000.00	\$4,000.00
40	04006 SP	Delineator, White (flexible)	EA	169	\$96.50	\$16,308.50	\$100.00	\$16,900.00	\$85.00	\$14,365.00
41	04006 SP	Delineator, Yellow (flexible)	EA	84	\$96.50	\$8,106.00	\$100.00	\$8,400.00	\$85.00	\$7,140.00
42	04006 SP	Delineator, Red	EA	67	\$96.50	\$6,465.50	\$100.00	\$6,700.00	\$60.00	\$4,020.00
43	04007 SP	Force Account	\$	130,000	\$1.00	\$130,000.00	\$1.00	\$130,000.00	\$1.00	\$130,000.00

TOTALS:

\$5,189,321.50

\$5,838,156.80

\$7,005,921.00

PART III: PROPOSAL

COUNTY ROAD 142 RECONSTRUCTION

BIDS CLOSE 2:00 P.M., MARCH 20, 2024

This Bid is submitted to:

Laramie County Public Works
Ms. Molly Bennett, Director
13797 Prairie Center Circle
Cheyenne, Wyoming 82009

The undersigned Bidder proposes and, if this Bid is accepted, agrees to enter into an Agreement with Owner in the form included in the Contract Documents, to complete all Work as specified or indicated in the Contract Documents for the Contract Price and within the Contract Time indicated in this Bid and in accordance with the Contract Documents.

Bidder accepts all terms and conditions of the Instructions to Bidders, including without limitation those dealing with the disposition of Bid Security. This bid will remain open for sixty (60) days after the day of Bid Opening. Bidder will sign the Agreement and submit the Contract Security and other documents required by the Contract Documents within fifteen (15) days after the date of Owner's Notice of Award.

In submitting this Bid, Bidder represents, as more fully set forth in the Agreement, that:

- (a) Bidder has examined copies of all the Contract Documents and of the following addenda (if none, so state):

Addendum No.	Addendum Date
<u>Addendum #1</u>	<u>2/26/2024</u>
<u>Addendum #2</u>	<u>3/11/2024</u>
<u> </u>	<u> </u>

(receipt of all of which is hereby acknowledged) and copies of the Advertisement or Invitation to Bid and the Instructions to Bidders;

- (b) Bidder has examined the site and locality where the Work is to be performed, the legal requirements (federal, state, and local laws, ordinances, rules, and regulations) and the conditions affecting costs, progress or performance of the Work and has made such independent investigations as Bidder deems necessary; and
- (c) This Bid is genuine and not made in the interest of or on behalf of any undisclosed person, firm or corporation and is not submitted in conformity with any agreement or rules of any group, association, organization or corporation; Bidder has not directly or indirectly induced or solicited any other Bidder to submit a false or sham Bid; Bidder has not

solicited or induced any person, firm or a corporation to refrain from bidding; and Bidder has not sought by collusion to obtain any advantage over any other Bidder or over Owner.

Bidder will complete the Work in accordance with the following Proposal Schedules. It is understood that the Owner has the right to reject any and all bids, also that the Owner may accept any or all Proposal Schedules. The Owner reserves the right to reduce quantities or eliminate items listed on the bid schedule in order for the project to meet the budget. The Owner reserves the right to increase or decrease the limits and/or scope of the project to better utilize allocated funds.

Bidder agrees that the Work will be substantially completed on or before the dates or within the number of working days indicated in the Agreement.

Bidder accepts the provisions of the Agreement as to Liquidated Damages in the event of failure to complete the Work on time.

The following is a list of documents that are included with and made a condition of this Bid:

- (a) This bid proposal completed and signed including acknowledgment of all addenda, if any.
- (b) Required Bid Security in the form of a signed Bid Bond, certified check, or cashier's check in the amount of not less than five percent (5%) of the total sum bid for all schedules.
- (c) Signed itemized bid sheet.
- (d) A list of all subcontractors and suppliers.

Communications concerning this bid shall be addressed to the address of Bidder indicated on page III-3 or III-4.

SUBMITTED THIS 20th DAY OF March, 2024.

(Bidder must sign in appropriate block below or on page III-4.)
(UNSIGNED BIDS WILL NOT BE ACCEPTED.)

A SOLE PROPRIETORSHIP

By _____

Doing Business As: _____

Business Address: _____

Telephone Number: (____) _____

A PARTNERSHIP

(Firm Name)

By: _____
(General Partner)

Business Address: _____

Telephone Number: (____) _____

(Signature forms for a Corporation or Joint Venture are on next page.)

SUBMITTED THIS 20th DAY OF March, 2024.

(Bidder must sign in appropriate block below or on page III-3.)
(UNSIGNED BIDS WILL NOT BE ACCEPTED.)


A CORPORATION

Simon Contractors
(Corporation Name)

Wyoming
(State of Incorporation)

By: 
(Name of Person Authorized to Sign)

Region Manager
(Title)

Attest: 
(Secretary)

Business Address: 6215 Clear Creek Parkway
Cheyenne, WY 82007

(Corporate Seal)

Telephone Number: (307) 772-3260

A JOINT VENTURE

By: _____

Address: _____

By: _____

Address: _____

By: _____

Address: _____

(Each party to a joint venture must sign. The manner of signing for each individual, partnership, and corporation that is a party to the joint venture should be in the manner indicated above. Provide additional sheets as necessary for additional members of a Joint Venture.)

ITEMIZED BID SHEET (Addendum 2)

PROJECT: COUNTY ROAD 142 RECONSTRUCTION

BASE BID – Revised March 11, 2024 (1 OF 3)

Item No.	Specification Section	Description	Unit	Estimated Quantity	Unit Price	Total Cost
1	04001 SP	Mobilization	LS	1	\$ 203,000.00	\$ 203,000.00
2	N/A	Bonds and Insurance	LS	1	\$ 24,500.00	\$ 24,500.00
3	04002 SP	Traffic Control and Site Safety	LS	1	\$ 171,200.00	\$ 171,200.00
4	04003 SP	Quality Control Testing	LS	1	\$ 35,500.00	\$ 35,500.00
5	N/A	Utility Potholing	EA	26	\$ 1,000.00	\$ 26,000.00
6	Addendum 2	Variable Message Signs (VMS)	DAY	90	\$ 140.00	\$ 12,600.00
7	Addendum 2	Flagging	HR	500	\$ 48.00	\$ 24,000.00
8	Addendum 2	Pilot Car	DAY	60	\$ 850.00	\$ 51,000.00
9	Addendum 2	Motor Grader Hours	HR	150	\$ 275.00	\$ 41,250.00
10	02050 SP	Remove Culvert	LF	1170	\$ 29.00	\$ 33,930.00
11	04006 SP	Remove Delineators	LS	1	\$ 107.00	\$ 107.00
12	02805 SP	Remove Sign (return to owner)	EA	10	\$ 273.00	\$ 2,730.00
13	02805	Remove & Reset Sign	EA	18	\$ 778.00	\$ 14,004.00
14	02050	Remove Concrete Approach	SY	100	\$ 36.50	\$ 3,650.00
15	02075 SP	Transition Section	EA	2	\$ 2,700.00	\$ 5,400.00
16	04004 SP	Full Depth Reclamation	SY	88000	\$ 2.00	\$ 176,000.00
17	04004 SP	Stabilized Full Depth Reclamation	SY	2400	\$ 12.00	\$ 28,800.00

COUNTY ROAD 142 RECONSTRUCTION ♦ LARAMIE COUNTY, WY

ITEMIZED BID SHEET (ADDENDUM 2)

PROJECT: County ROAD 142 RECONSTRUCTION

BASE BID -- Revised March 11, 2024 (2 OF 3)

18	Addendum 2	Topsoil Stripping	LS	1	\$	67,000.00	\$	67,000.00
19	02210	Unclassified Excavation	CY	31000	\$	9.70	\$	300,700.00
20	02231 SP	Crushed Base, 6" (for approaches)	Ton	700	\$	29.50	\$	20,650.00
21	02231 SP	Crushed Base, 6" (for mainline roads)	Ton	36000	\$	29.50	\$	1,062,000.00
22	02231 SP	Crushed Base, 6" (surfacing)	Ton	820	\$	29.50	\$	24,190.00
23	02190 SP	Crushed Base (shoulder material)	Ton	800	\$	35.00	\$	28,000.00
24	02512 SP	Plant Mix Bit. Pavement, 3" (for approaches)	Ton	400	\$	223.00	\$	89,200.00
25	02512 SP	Plant Mix Bit. Pavement, 4" (for mainline roads)	Ton	22400	\$	102.50	\$	2,296,000.00
26	02776 SP	Concrete Approach, 6"	SY	65	\$	148.00	\$	9,620.00
27	02725	18" CMP Culvert	LF	1070	\$	67.00	\$	71,690.00
28	02725	24" CMP Culvert	LF	860	\$	87.00	\$	74,820.00
29	0	36" CMP Culvert	LF	150	\$	131.00	\$	19,650.00
30	02725	18" CMP FES	EA	38	\$	402.00	\$	15,276.00
31	02725	24" CMP FES	EA	24	\$	615.25	\$	14,766.00
32	02725	36" CMP FES	EA	4	\$	1,605.00	\$	6,420.00
33	02805 SP	Sign, Single Post	EA	11	\$	909.50	\$	10,004.50
34	02805 SP	Sign, Double Post	EA	2	\$	1,350.00	\$	2,700.00
35	02805 SP	Stop Sign with Solar Powered Flashing Beacon	EA	2	\$	6,420.00	\$	12,840.00
36	2900	Dryland Seed	Acre	16.3	\$	1,450.00	\$	23,635.00
37	04005 SP	Striping, Edge Line	Mile	9.7	\$	1,450.00	\$	14,065.00

COUNTY ROAD 142 RECONSTRUCTION LARAMIE CNTY, WY

BASE BID – Revised March 11, 2024 (3 OF 3)

38	04005 SP	Striping, Centerline	Mile	4.88	\$ 1,050.00	\$ 5,124.00
39	04005 SP	Railroad Crossing Markings	EA	2	\$ 3,210.00	\$ 6,420.00
40	04006 SP	Delineator, White (flexible)	EA	169	\$ 96.50	\$ 16,308.50
41	04006 SP	Delineator, Yellow (flexible)	EA	84	\$ 96.50	\$ 8,106.00
42	04006 SP	Delineator, Red	EA	67	\$ 96.50	\$ 6,465.50
43	04007 SP	Force Account	\$	130000	\$ 1.00	\$ 130,000.00
						\$ 5,189,321.50

Total Base Bid:

Signature of Bidder:

Print Name: Rob Meidinger

Company Name:

Simon Contractors

Date: 3/20/2024

Note: The Owner reserves the right to reduce quantities or eliminate items listed on the bid schedule in order for the project to meet the budget.

COUNTY ROAD 142 RECONSTRUCTION LARAMIE CONTY, WY

LIST OF SUBCONTRACTORS AND MATERIAL SUPPLIERS			
Work	Subcontractor or Material Supplier	City, State	% of Work
Earthwork, Base, CMP/FES, Topsoil	Pine Bluffs Gravel and Excavating Inc	Pine Bluffs, WY	27%
FDR	ARS Companies	Wheat Ridge, CO	2%
Traffic Control/Striping	S&L Industrial	Cowley, WY	7%
Testing	JB Engineers	Cheyenne, WY	1%
Seeding	Rocky Mountain Reclamation	Laramie, WY	1%

Note: A list of subcontractors and material suppliers proposed for this project shall be completed and submitted with the bid. Use additional sheets if necessary.

PROJECT: COUNTY ROAD 142 RECONSTRUCTION

KNOW ALL MEN BY THESE PRESENTS, that Simon Contractors, as Bidder, and, Liberty Mutual Insurance Company, as Surety, a corporation duly organized under the laws of the State of MA and authorized to do business within the State of Wyoming, are held and firmly bound unto Laramie County, Wyoming, in the full and just sum of Five Percent of Amount Bid (\$ 5%), lawful money of the United States, for the payment of which sum, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and as-signs, jointly and severally, firmly by these presents.

WHEREAS, said Principal is herewith submitting a Proposal for the COUNTY ROAD 142 RECONSTRUCTION, and Laramie County, Wyoming, has required as a condition for submitting said Proposal, that said Principal deposit specified Bid Security in an amount not less than five percent (5%) of the amount of said Proposal, conditioned that in event of failure of Principal to execute the Contract and furnish the required performance and payment bonds if the Contract is awarded to said principal, that said sum be paid immediately to Laramie County, Wyoming as liquidated damages, and not as penalty, for the Principal's failure to perform.

The condition of this obligation is such that if the aforesaid Principal will, within the time required, enter into a formal contract and give such bonds as are specified in the bidding documents with surety acceptable to Laramie County; or if Principal shall fail to do so, pay to Laramie County the sum determined herein as liquidated damages and not as a penalty, then this obligation shall be void; otherwise it shall remain in full force and effect.

IN WITNESS WHEREOF, the above bonded parties have executed this instrument under their seals this 7th day of March, 20 24.

BIDDER

SURETY

Simon Contractors (Seal)

Liberty Mutual Insurance Company (Seal)

By: [Signature]
Signature and Title

REGINA HAWAGUN

By: [Signature]
Signature and Title Michelle Anne McMahon, Attorney-in-Fact
(Attach Power of Attorney)

Attest: _____
Signature and Title

Attest: [Signature]
Signature and Title Imani Schley, Witness



This Power of Attorney limits the acts of those named herein, and they have no authority to bind the Company except in the manner and to the extent herein stated.

Liberty Mutual Insurance Company
The Ohio Casualty Insurance Company
West American Insurance Company

Certificate No: **8210646 - 985949**

POWER OF ATTORNEY

KNOWN ALL PERSONS BY THESE PRESENTS: That The Ohio Casualty Insurance Company is a corporation duly organized under the laws of the State of New Hampshire, that Liberty Mutual Insurance Company is a corporation duly organized under the laws of the State of Massachusetts, and West American Insurance Company is a corporation duly organized under the laws of the State of Indiana (herein collectively called the "Companies"), pursuant to and by authority herein set forth, does hereby name, constitute and appoint, Connor Wolpert, Doritza Mojica, Gentry Stewart, Jennifer Godere, Jonathan Gleason, Joshua Sanford, Kathryn Pryor, Kyle Williams, Michelle Anne McMahon, Nicholas Miller, Richard Hackner, Robyn Salley, Sarah Murtha

all of the city of Hartford state of CT each individually if there be more than one named, its true and lawful attorney-in-fact to make, execute, seal, acknowledge and deliver, for and on its behalf as surety and as its act and deed, any and all undertakings, bonds, recognizances and other surety obligations, in pursuance of these presents and shall be as binding upon the Companies as if they have been duly signed by the president and attested by the secretary of the Companies in their own proper persons.

IN WITNESS WHEREOF, this Power of Attorney has been subscribed by an authorized officer or official of the Companies and the corporate seals of the Companies have been affixed thereto this 22nd day of August, 2023.



Liberty Mutual Insurance Company
The Ohio Casualty Insurance Company
West American Insurance Company

By: David M. Carey
David M. Carey, Assistant Secretary

State of PENNSYLVANIA ss
County of MONTGOMERY

On this 22nd day of August, 2023 before me personally appeared David M. Carey, who acknowledged himself to be the Assistant Secretary of Liberty Mutual Insurance Company, The Ohio Casualty Company, and West American Insurance Company, and that he, as such, being authorized so to do, execute the foregoing instrument for the purposes therein contained by signing on behalf of the corporations by himself as a duly authorized officer.

IN WITNESS WHEREOF, I have hereunto subscribed my name and affixed my notarial seal at Plymouth Meeting, Pennsylvania, on the day and year first above written.



Commonwealth of Pennsylvania - Notary Seal
Teresa Pastella, Notary Public
Montgomery County
My Commission expires March 26, 2025
Commission number 1126044
Member, Pennsylvania Association of Notaries

By: Teresa Pastella
Teresa Pastella, Notary Public

This Power of Attorney is made and executed pursuant to and by authority of the following By-laws and Authorizations of The Ohio Casualty Insurance Company, Liberty Mutual Insurance Company, and West American Insurance Company which resolutions are now in full force and effect reading as follows:

ARTICLE IV - OFFICERS: Section 12. Power of Attorney.

Any officer or other official of the Corporation authorized for that purpose in writing by the Chairman or the President, and subject to such limitation as the Chairman or the President may prescribe, shall appoint such attorneys-in-fact, as may be necessary to act in behalf of the Corporation to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations. Such attorneys-in-fact, subject to the limitations set forth in their respective powers of attorney, shall have full power to bind the Corporation by their signature and execution of any such instruments and to attach thereto the seal of the Corporation. When so executed, such instruments shall be as binding as if signed by the President and attested to by the Secretary. Any power or authority granted to any representative or attorney-in-fact under the provisions of this article may be revoked at any time by the Board, the Chairman, the President or by the officer or officers granting such power or authority.

ARTICLE XIII - Execution of Contracts: Section 5. Surety Bonds and Undertakings.

Any officer of the Company authorized for that purpose in writing by the chairman or the president, and subject to such limitations as the chairman or the president may prescribe, shall appoint such attorneys-in-fact, as may be necessary to act in behalf of the Company to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations. Such attorneys-in-fact subject to the limitations set forth in their respective powers of attorney, shall have full power to bind the Company by their signature and execution of any such instruments and to attach thereto the seal of the Company. When so executed such instruments shall be as binding as if signed by the president and attested by the secretary.

Certificate of Designation - The President of the Company, acting pursuant to the Bylaws of the Company, authorizes David M. Carey, Assistant Secretary to appoint such attorneys-in-fact as may be necessary to act on behalf of the Company to make, execute, seal, acknowledge and deliver as surety any and all undertakings, bonds, recognizances and other surety obligations.

Authorization - By unanimous consent of the Company's Board of Directors, the Company consents that facsimile or mechanically reproduced signature of any assistant secretary of the Company, wherever appearing upon a certified copy of any power of attorney issued by the Company in connection with surety bonds, shall be valid and binding upon the Company with the same force and effect as though manually affixed.

I, Renee C. Llewellyn, the undersigned, Assistant Secretary, The Ohio Casualty Insurance Company, Liberty Mutual Insurance Company, and West American Insurance Company do hereby certify that the original power of attorney of which the foregoing is a full, true and correct copy of the Power of Attorney executed by said Companies, is in full force and effect and has not been revoked.

IN TESTIMONY WHEREOF, I have hereunto set my hand and affixed the seals of said Companies this 7th day of March, 2024.



By: Renee C. Llewellyn
Renee C. Llewellyn, Assistant Secretary

Not valid for mortgage, note, loan, letter of credit, currency rate, interest rate or residual value guarantees.

For bond and/or Power of Attorney (POA) verification inquiries, please call 610-832-8240 or email HOSUR@libertymutual.com



LIBERTY MUTUAL INSURANCE COMPANY

Financial Statement – December 31, 2022

Assets		Liabilities	
Cash and Bank Deposits	\$3,908,755,039	Unearned Premiums	\$10,133,358,204
*Bonds — U.S Government	3,451,999,931	Reserve for Claims and Claims Expense	27,953,643,316
*Other Bonds	18,862,255,155	Funds Held Under Reinsurance Treaties	368,610,620
*Stocks	19,372,953,698	Reserve for Dividends to Policyholders	1,379,296
Real Estate	190,092,373	Additional Statutory Reserve	197,278,000
Agents' Balances or Uncollected Premiums	7,929,876,358	Reserve for Commissions, Taxes and	
Accrued Interest and Rents	166,740,412	Other Liabilities	9,206,000,954
Other Admitted Assets	15,968,062,977	Total	\$47,860,270,390
Total Admitted Assets	<u>\$69,850,735,943</u>	Special Surplus Funds	\$195,696,103
		Capital Stock	10,000,075
		Paid in Surplus	13,324,803,036
		Unassigned Surplus	8,459,966,339
		Surplus to Policyholders	21,990,465,553
		Total Liabilities and Surplus	<u>\$69,850,735,943</u>



* Bonds are stated at amortized or investment value; Stocks at Association Market Values.
The foregoing financial information is taken from Liberty Mutual Insurance Company's financial statement filed with the state of Massachusetts Department of Insurance.

I, TIM MIKOLAJEWSKI, Assistant Secretary of Liberty Mutual Insurance Company, do hereby certify that the foregoing is a true, and correct statement of the Assets and Liabilities of said Corporation, as of December 31, 2022, to the best of my knowledge and belief.

IN WITNESS WHEREOF, I have hereunto set my hand and affixed the seal of said Corporation at Seattle, Washington, this 8th day of March 2023.

TAMikolajewski

Assistant Secretary



STATE OF WYOMING

CERTIFICATE OF RESIDENCY



Contractor Number: 0396

SIMON CONTRACTORS

HAS BEEN GRANTED RESIDENCY STATUS PURSUANT TO WYOMING STATUTE 16-6-101, AS AMENDED. FIVE PERCENT PREFERENCE SHALL BE ALLOWED WHEN BIDDING ON ANY PUBLIC WORKS CONTRACT FOR A PERIOD OF ONE (1) YEAR FROM THE DATE CERTIFICATION IS GRANTED.

GRANTED THIS 5TH DAY of JULY TWO THOUSAND AND 23

A handwritten signature in black ink, appearing to read "Michele Johnson".


Michele Johnson, Program Manager

EXPIRATION DATE: 7/4/2024



To verify the authenticity of the certificate,
please contact our office at 307-777-7261 or visit
wyomingworkforce.org/businesses/labor/info

CERTIFICATE SERIAL NUMBER: 0507202339

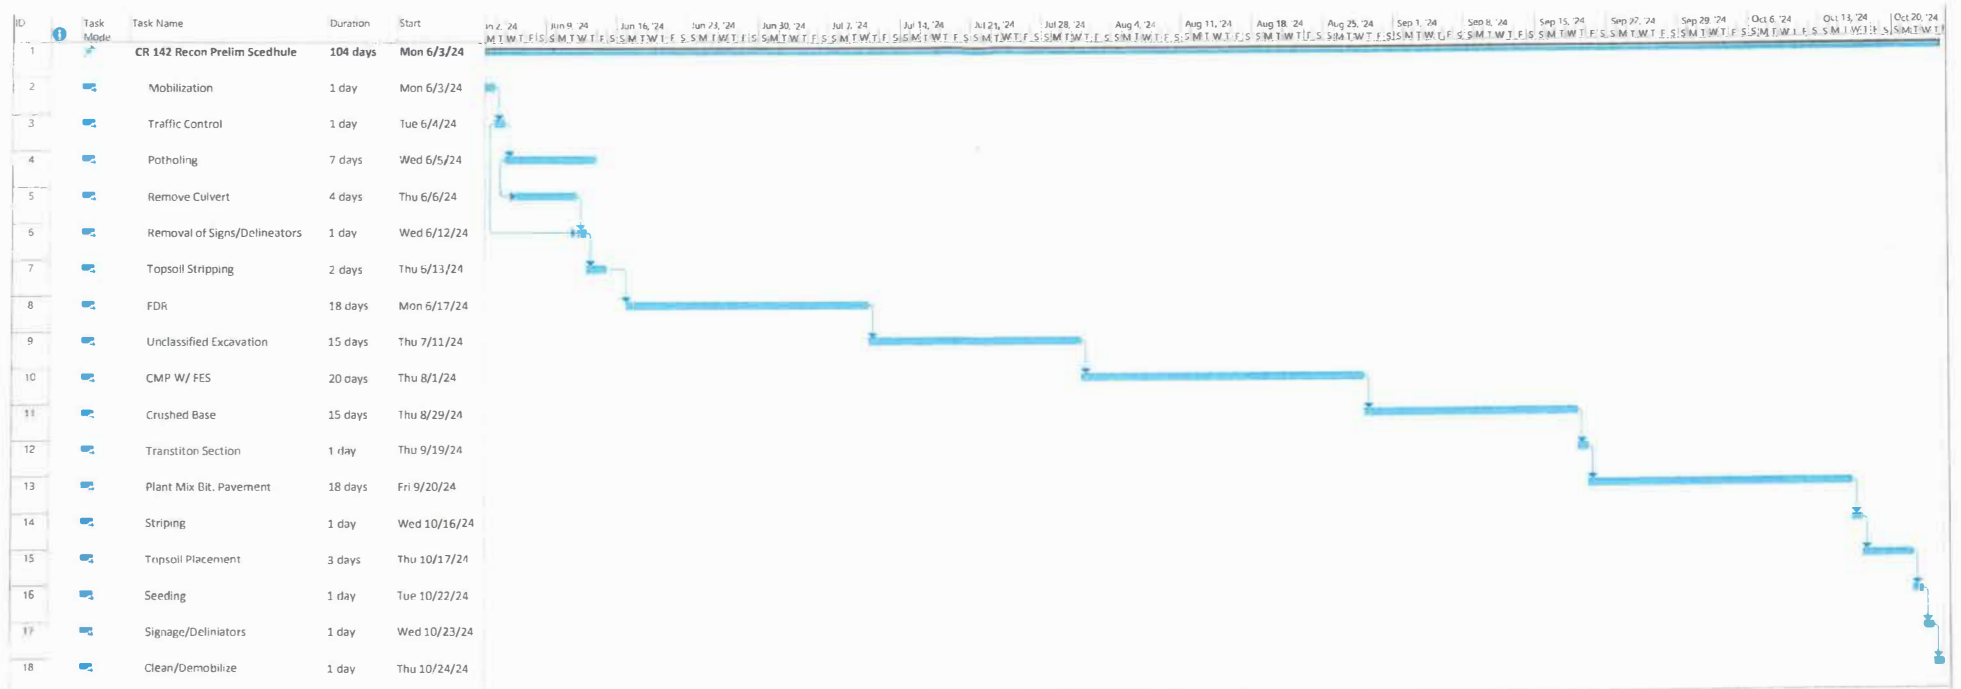

Project: CR 142 Recon Bid Sche
Date: Wed 3/20/24

